
VegaHealth

Baptist Health Kentucky & Indiana: Proposed Project Plan

Discussion Document | October 9, 2026

Preliminary Project Overview

Dependency

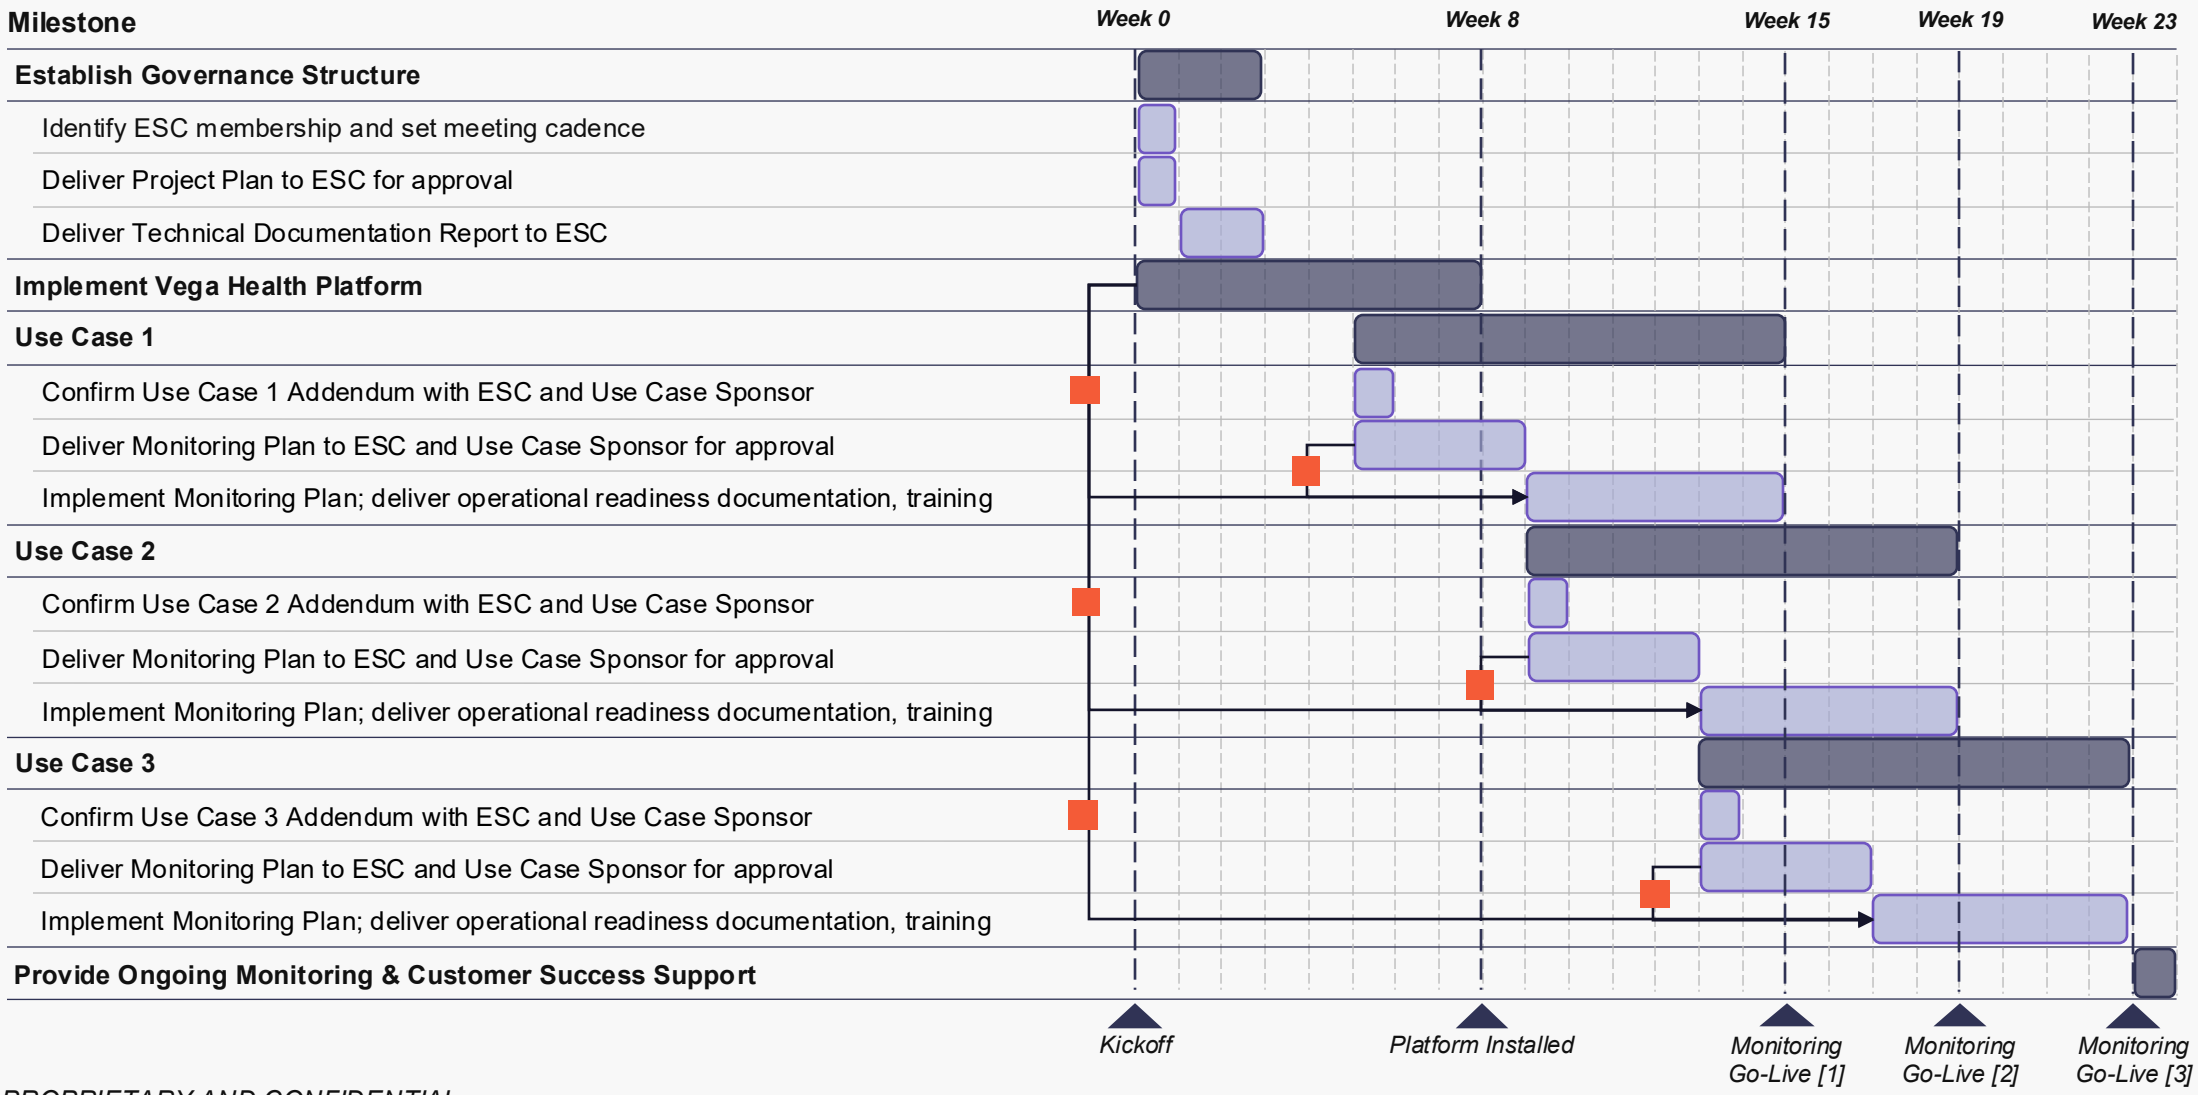

Preliminary Staffing Model: Baptist Health & Vega Health

**Estimates only as informed by previous customer implementations; Vega Health will flex resources, as needed, to meet timely execution of Deliverables*

Resource	Effort & Duration	Role & Responsibilities
Executive Steering Committee		
Mark Sendak [Executive]	0.05 FTE [2 hours/week], 6 months	ESC co-chair
Joanne Kim [Executive]	0.2 FTE [8 hours/week], 6 months	Vega Health primary partnership contact
Baptist Health Executive Champion	2 hours/month, 6 months	Baptist Health engagement decision-maker
Baptist Health Technology Lead	0.05 FTE [2 hours/week], 6 months	Technical leader supporting resource allocation & approvals
Baptist Health Project Lead	0.1 FTE [4 hours/week], 6 months	Baptist Health project manager supporting day-to-day operations
Platform Implementation		
Vega Health Forward Deployed Engineer	1 FTE [40 hours/week], 6 weeks	Coordinates Platform installation [e.g., site adapter, data pipeline]
Baptist Health Health IT Analyst	0.2 FTE [8 hours/week], 2 weeks	Supports FHIR and HL7 integrations and Platform maintenance
Baptist Health Infrastructure & Storage Architect	0.25 FTE [10 hours/week], 2 weeks	Supports environment provisioning and change management
Baptist Health Information Security Analyst	0.2 FTE [8 hours/week], 1 week	Supports security review and validation
Baptist Health Data Analyst	0.2 FTE [8 hours/week] 2 weeks	Supports data governance compliance and reporting
Baptist Health Networking Analyst	0.25 FTE [10 hours/week], 1 week	Supports networking, DNS, and VPN configuration
Monitoring Use Cases		
Vega Health Engagement Manager	0.5 FTE [20 hours/week], 18 weeks	Manages day-to-day operations, deliverables, and coordination
Vega Health AI Scientist	0.5 FTE [20 hours/week], 18 weeks	Manages scope, onboarding, and operationalization of Use Case monitoring
Use Case Sponsors	0.1 FTE [4 hours/week], 6 weeks	Leaders owning Use Case model and outcomes
Use Case Subject Experts	0.1 FTE [4 hours/week], 6 weeks	Provide institutional clinical/operational expertise for each Use Case model
End-Users	0.1 FTE [4 hours/week], 6 weeks	Provide input on workflow; utilize monitoring outputs to fulfill roles

Preliminary RACI Matrix

	Executive Steering Committee				Platform Implementation		Monitoring Use Cases			
	VH Executive	BH Exec. Champion	BH Tech Lead	BH Project Lead	VH Engineers	BH Tech Resources	VH Project Lead (EM)	VH AI Scientist	BH Use Case Lead	BH Expert & End-User
Establish Governance Structure										
Identify ESC membership and set meeting cadence	I	A	C	R						
Deliver Project Plan to ESC for approval	A R	C	C	C						
Deliver Technical Documentation Report to ESC	A R	C	C	C						
Implement Vega Health Platform										
Complete infrastructure & Entra setup					C	R				
Complete Data Pipeline Integration					C	R				
Platform Software Installation					R	C				
Onboard Use Cases to Platform					R	C				
Monitoring Use Cases										
Confirm Use Case Addendum with ESC and Use Case Sponsor							A	R	C	I
Deliver Monitoring Plan to ESC and Use Case Sponsor for approval							A	R	C	I
Implement Monitoring Plan; deliver documentation, training							A	R	C	C
Provide Ongoing Monitoring & Customer Success Support										

Customer Success

Customer Success Dimensions	Customer Success Dimensions
Platform	
Technical Documentation for Platform	Deliver full documentation, installation guides, runbooks, and configurations to operate the Vega Health Platform
Platform Onboarding & Training	Provide Platform owners and end-users with training to support successful operation and use
Technical Support (e.g., email inbox, dedicated business hours phone availability for escalation)	Provide Platform owners and end-users with a ticket and support inbox, as well as phone contact for a dedicated account representative
Monitoring Use Cases	
Monitoring Plan [per use case]	Deliver deliver a Monitoring Plan with key metrics, alerts & workflows, and audiences/accountable parties
Operational Readiness Trainings [per use case]	Deliver operational readiness trainings for each Use Case Sponsor, end-users, and other stakeholders
Monitoring Workflow Enablement for Use Case Sponsors, End-Users	Support the development and success of Use Case-specific workflows leveraging Vega Health capabilities
Technical Support (e.g., email inbox, dedicated business hours phone availability for escalation)	Provice Use Case Sponsors and end-users with a ticket and support inbox, as well as phone contact for a dedicated account representative

Vega Health SLAs

Vega Health will observe SLAs for Critical, High, Medium, and Low severity tickets based on internal Baptist Health uptime requirements and policies. If no such policies or definitions exist, Vega Health will present formal SLAs for approval to the ESC as part of the Project Plan.

All tickets will receive a same-day acknowledgement and an estimated timeline to resolution consistent with agreed-upon SLAs.
